


What's Achieved: Dismantled Kitchen Area

Breaking down to build up

- Demolition of the industrial kitchen is completed on schedule and with minimal disruption. (Apr-May)
- Noise management: KLU received only a few complaints during the exam period. It was resolved quickly.
- **Next step:** Dust barrier installed in the foyer by the end of June.

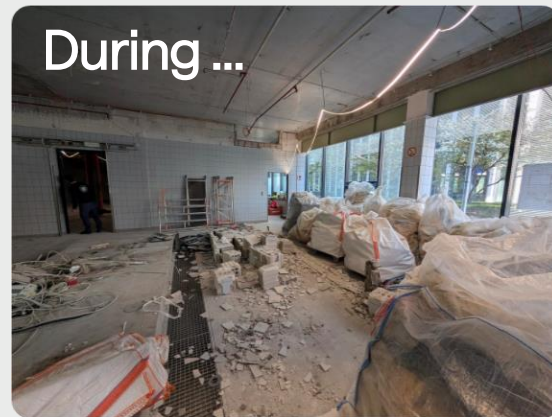

And after demolition of the kitchen ...



Making Space for... More & Modernized Lecture Rooms

New teaching spaces

Ground Floor with
6 Rooms:

- Arena Teaching
- Other new lecture rooms
- Flexible layouts (folding walls)
- Adaptable for different class sizes



What's Ahead: Renovations during Summer

Making the best of the semester break



Summer renovations start in **July**:

- less students on Campus – no impact on lectures
- some staff on vacation – minimize work disruption

July-August 2026:

- Ground floor: preparation for new lecture rooms
- Lower basement: new Student Lounge and Gym construction begins

During Phase 1 (Jun 26- Jan 27)

- Temporary closure: Gym out of service June-December 2026 (using summer break strategically)
- Campus remains fully operational for teaching and learning

How You Can Help: Communicating in the right channels

Your feedback helps us adjust quickly.

For noise complaints, disruptions, or feedback:

servicedesk@klu.org

For event organizers among staff, faculty and students:

Share upcoming events early with Facility Management so that we can coordinate with construction teams.



Thank you for your patience and collaboration!

Timeline Campus Hamburg

Preparation

Early Apr 2026 - End of Jun 2026

- The catering kitchen behind the old cafeteria on the ground floor gets dismantled.

End of June 2026

- A protective dust wall is set up in the Foyer.

Construction Phase 1

Jul 2026 - Jan 2027

- Construction work on the ground floor to prepare for the new lecture rooms.
- Another construction zone being installed on the first basement for the new Student Lounge and Gym.

Construction Phase 2

Feb 2027 – Jun 2027

- Setting up the new library and campus café on the ground floor.
- Another construction zone on the first and second floor.

Construction Phase 3

Feb - Sep 2027


- Setting up the second-floor breakout rooms and new lecture rooms.

Sep 2027

- Grand Opening


On The Way to a Redesigned Campus

Students:
MOODLE



- Recommendation to use the latest versions of Firefox | Google Chrome
- Access via the link (no log-in needed anymore)
- If it doesn't work the first time, try again. Still not successful? Submit a ticket to: servicedesk@klu.org.

Staff:
KLU HUB



Feedback / Questions?

We hear you! Share via servicedesk@klu.org.
